

# STREET CUT PERMIT

CITY OF SILOAM SPRINGS, ARKANSAS

PERMIT #:

DATE

## PART I: TO BE COMPLETED BY APPLICANT

APPLICANT

PHONE NO

ADDRESS

CELL NO

CONTRACTOR

PHONE NO

ADDRESS

CELL NO

LOCATION OF WORK

DESCRIPTION OF WORK

DESIRED START DATE

PARTIAL STREET CUT

YES

NO

IT IS UNDERSTOOD AND AGREED TO THAT ANY INSTALLATION OR WORK COVERED BY ANY PERMIT ISSUED AS A RESULT OF THIS APPLICATION IS SUBJECT TO STATE AND OR CITY RULES AND REGULATIONS PRESCRIBED BY THE CITY OF SILOAM SPRINGS. I FULLY UNDERSTAND THE ATTACHED STREET CUT/ ROAD BORE POLICY AND PROCEDURES AND AGREE TO COMPLY.

NAME

TITLE

SIGNATURE

DATE

## PART II : TO BE COMPLETED BY THE CITY OF SILOAM SPRINGS

**FEES:**  
(CHECK  
BOXES)

ADMIN. REVIEW FEE:

\$50.00

BOND RECEIVED:

INSPECT FEE: CUT

\$100.00

**TOTAL FEES PAID:**

BOND ISSUE DATE:

START DATE

NOTIFICATION DATE

BOND RELEASE DATE:

**APPROVALS:**

DATE

SIGNATURE

APPROVAL

CITY ENGINEER

JUSTIN BLAND

COMMENTS:

STREET SUPERINTENDENT

DENNIS KINDY

COMMENTS:

THE CITY OF SILOAM SPRINGS CONSTRUCTION MANAGER MUST BE NOTIFIED AND PRESENT ON SITE BEFORE ANY BASE MATERIALS OR BACK-FILL IS PLACED INTO THE TRENCH. PLEASE CALL THE PUBLIC WORKS DEPARTMENT AT (479) 238-0921, DURING NORMAL WORKING HOURS, TO SET UP AN INSPECTION TIME. NORMAL WORKING HOURS ARE FROM 8:00 AM TO 5:00 PM, MONDAY THROUGH FRIDAY. A STREET CUT REPAIR DETAIL CAN BE OBTAINED FROM THE PUBLIC WORKS OFFICE.

STREET CUT REPAIR  
INSPECTION

CONSTRUCTION/STREET MANAGER

ONE YEAR INSPECTION  
FOR BOND RELEASE:

CONSTRUCTION/STREET MANAGER

COMMENTS:

### STREET CUT PROCEDURES

1. No street cut shall take place until the application is completed and approval is granted by the City of Siloam Springs Engineering Department. Seven (7) days' notice is required prior to commencement of work. Total permit cost is \$150.00.
2. Prior to the issuance of a permit, the applicant shall post a surety bond, cash or irrevocable letter of credit in the sum of \$2,500.00 to be held by the City for a period of twenty-four (24) months.
3. Work zones meeting Manual on Uniform Traffic Control Devices (MUTCD) regulations must be set up at all street cut locations to ensure worker, traffic, and public safety.
4. If full street closure is required, the contract must notify the local newspaper seven (7) days prior to street closure so that the public will be aware of said closing. Permittee shall occupy or close the street only as specifically provided in the City issued permit.
5. The contractor is required to visibly mark and call for all utility locates from Arkansas One-Call at 1-800-482-8998 a minimum of 48 hours prior to commencement of work.
6. All street cuts must be visibly marked with painted or chalked lines and must be saw-cut on all sides to ensure smooth straight edges before any excavations begin.
7. The City of Siloam Springs Engineering Department must be notified before any aggregate base materials or back fill is placed into the trench. NO BACK-FILL MAY BE PLACED INTO AN OPEN TRENCH WITHOUT THE PRESENCE OF A MEMBER OF THE ENGINEERING DEPARTMENT. Please call the Engineering Department at 479-238-0927 during normal working hours to set up an inspection time. Normal working hours are from 8:00 am to 5:00 pm Monday through Friday. Any party needing to make an emergency street cut after hours must call Police Dispatch at 479-524-4118. A \$20.00 per hour charge will be assessed to all after hour call outs in addition to normal charges.
8. Compacted Class 7 Base or flowable back-fill (100-300 psi) is required for all back filling. Base material must be placed into trench in no more than 6-inch lifts and each lift must be mechanically compacted to a minimum of 95% density. (See Street Cut Repair Detail attachment for specifications.)
9. Contractor shall provide all labor, materials, shoring devices and equipment necessary for providing and maintaining a trench safety program that conforms with all Occupational Safety and Health Administration (OSHA) regulations and guidelines, as revised.
10. The party making the cut shall be responsible for any future settling of the street cut for a period of TWENTY-FOUR (24) months from the date the repair is completed.
11. The surety bond, cash, or irrevocable letter of credit on file with the City shall be returned to the applicant only after the City has conducted and passed the two (2) year inspection.

---


Customer Signature

---

Date

---

Company Represented

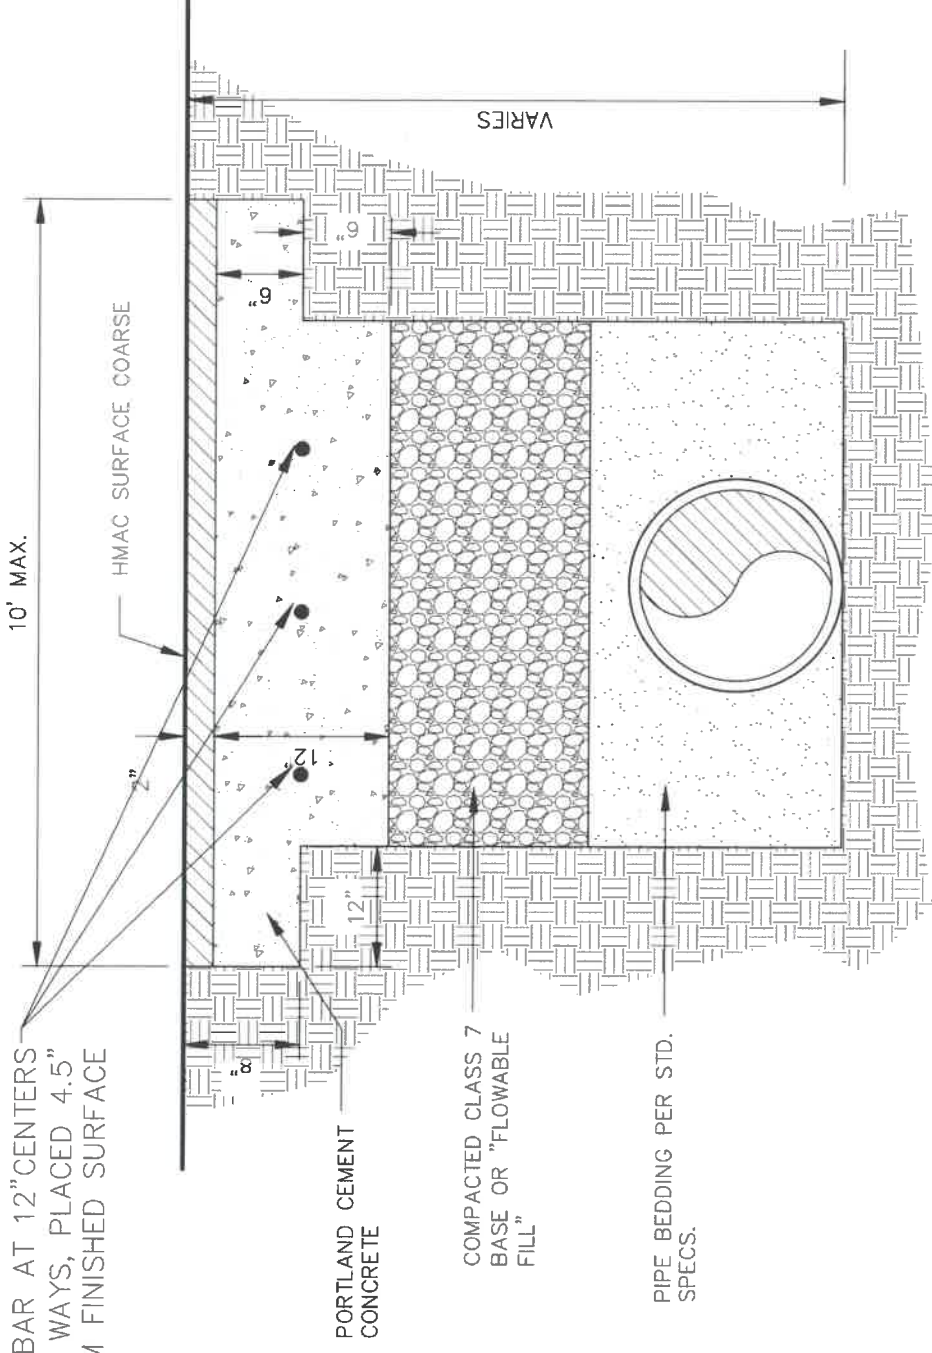

#3 REBAR AT 12" CENTERS BOTH WAYS, PLACED 4.5" FROM FINISHED SURFACE

PORTLAND CEMENT CONCRETE

COMPACTED CLASS 7 BASE OR "FLOWABLE FILL"

PIPE BEDDING PER STD. SPECS.

NOTE:  
AN ALTERNATIVE TO USING HM/MAC IS TO PLACE FULL DEPTH CONCRETE AND DYE SURFACE BLACK

# STREET REPAIR

N.T.S.
